


**YUCCA MESA & BUENA VISTA INTERSECTION IMPROVEMENT PROJECT**

Schedule as of 3/5/26  
90 working days

Project start: **Mon, 2/23/2026**  
Display week: **1**

TASK	ASSIGNED TO	PROGRESS	START	END
		0%	2/23/26	2/23/26
		0%	2/24/26	2/24/26
Mobilize survey and saw cut for curb/ pothole		0%	2/25/26	2/25/26
Begin demo and grade for concrete curb		0%	2/26/26	2/26/26
Finish grading for concrete curb		0%	2/27/26	2/27/26
		0%	3/2/26	3/2/26
Finish form work for curb		0%	3/2/26	3/2/26
Pour concrete curb		0%	3/3/26	3/3/26
Grade and form concrete cut off wall		0%	3/4/26	3/4/26
Pour concrete curb cut off wall		0%	3/5/26	3/5/26
Project maintenance and misc items		0%	3/6/26	3/6/26
		0%	3/9/26	3/9/26
Grade and form work for cut off wall/Geotech needed for compaction		0%	3/9/26	3/9/26
Pour cut off wall grade/backfill behind new curbs		0%	3/10/26	3/10/26
Set up traffic control closure for Thr-Sat work		0%	3/11/26	3/11/26
First Shift: Asphalt demo on Yucca Mesa Rd and Buena Vista Dr Second Shift: Cut dirt to grade prep subgrade		0%	3/12/26	3/12/26
First Shift: Geotech needed for subgrade compaction/ begin laying base Second Shift: Finish laying down base material, fine grade and compaction		0%	3/13/26	3/13/26
Asphalt Base pave and AC cap overlay/Install temp tabs /Open Road		0%	3/14/26	3/14/26
Project Maintenance		0%	3/16/26	3/16/26
Project Maintenance		0%	3/17/26	3/17/26
Project Maintenance		0%	3/18/26	3/18/26
Demobilize		0%	3/19/26	3/19/26
Demobilize/Schedule Striping		0%	3/20/26	3/20/26

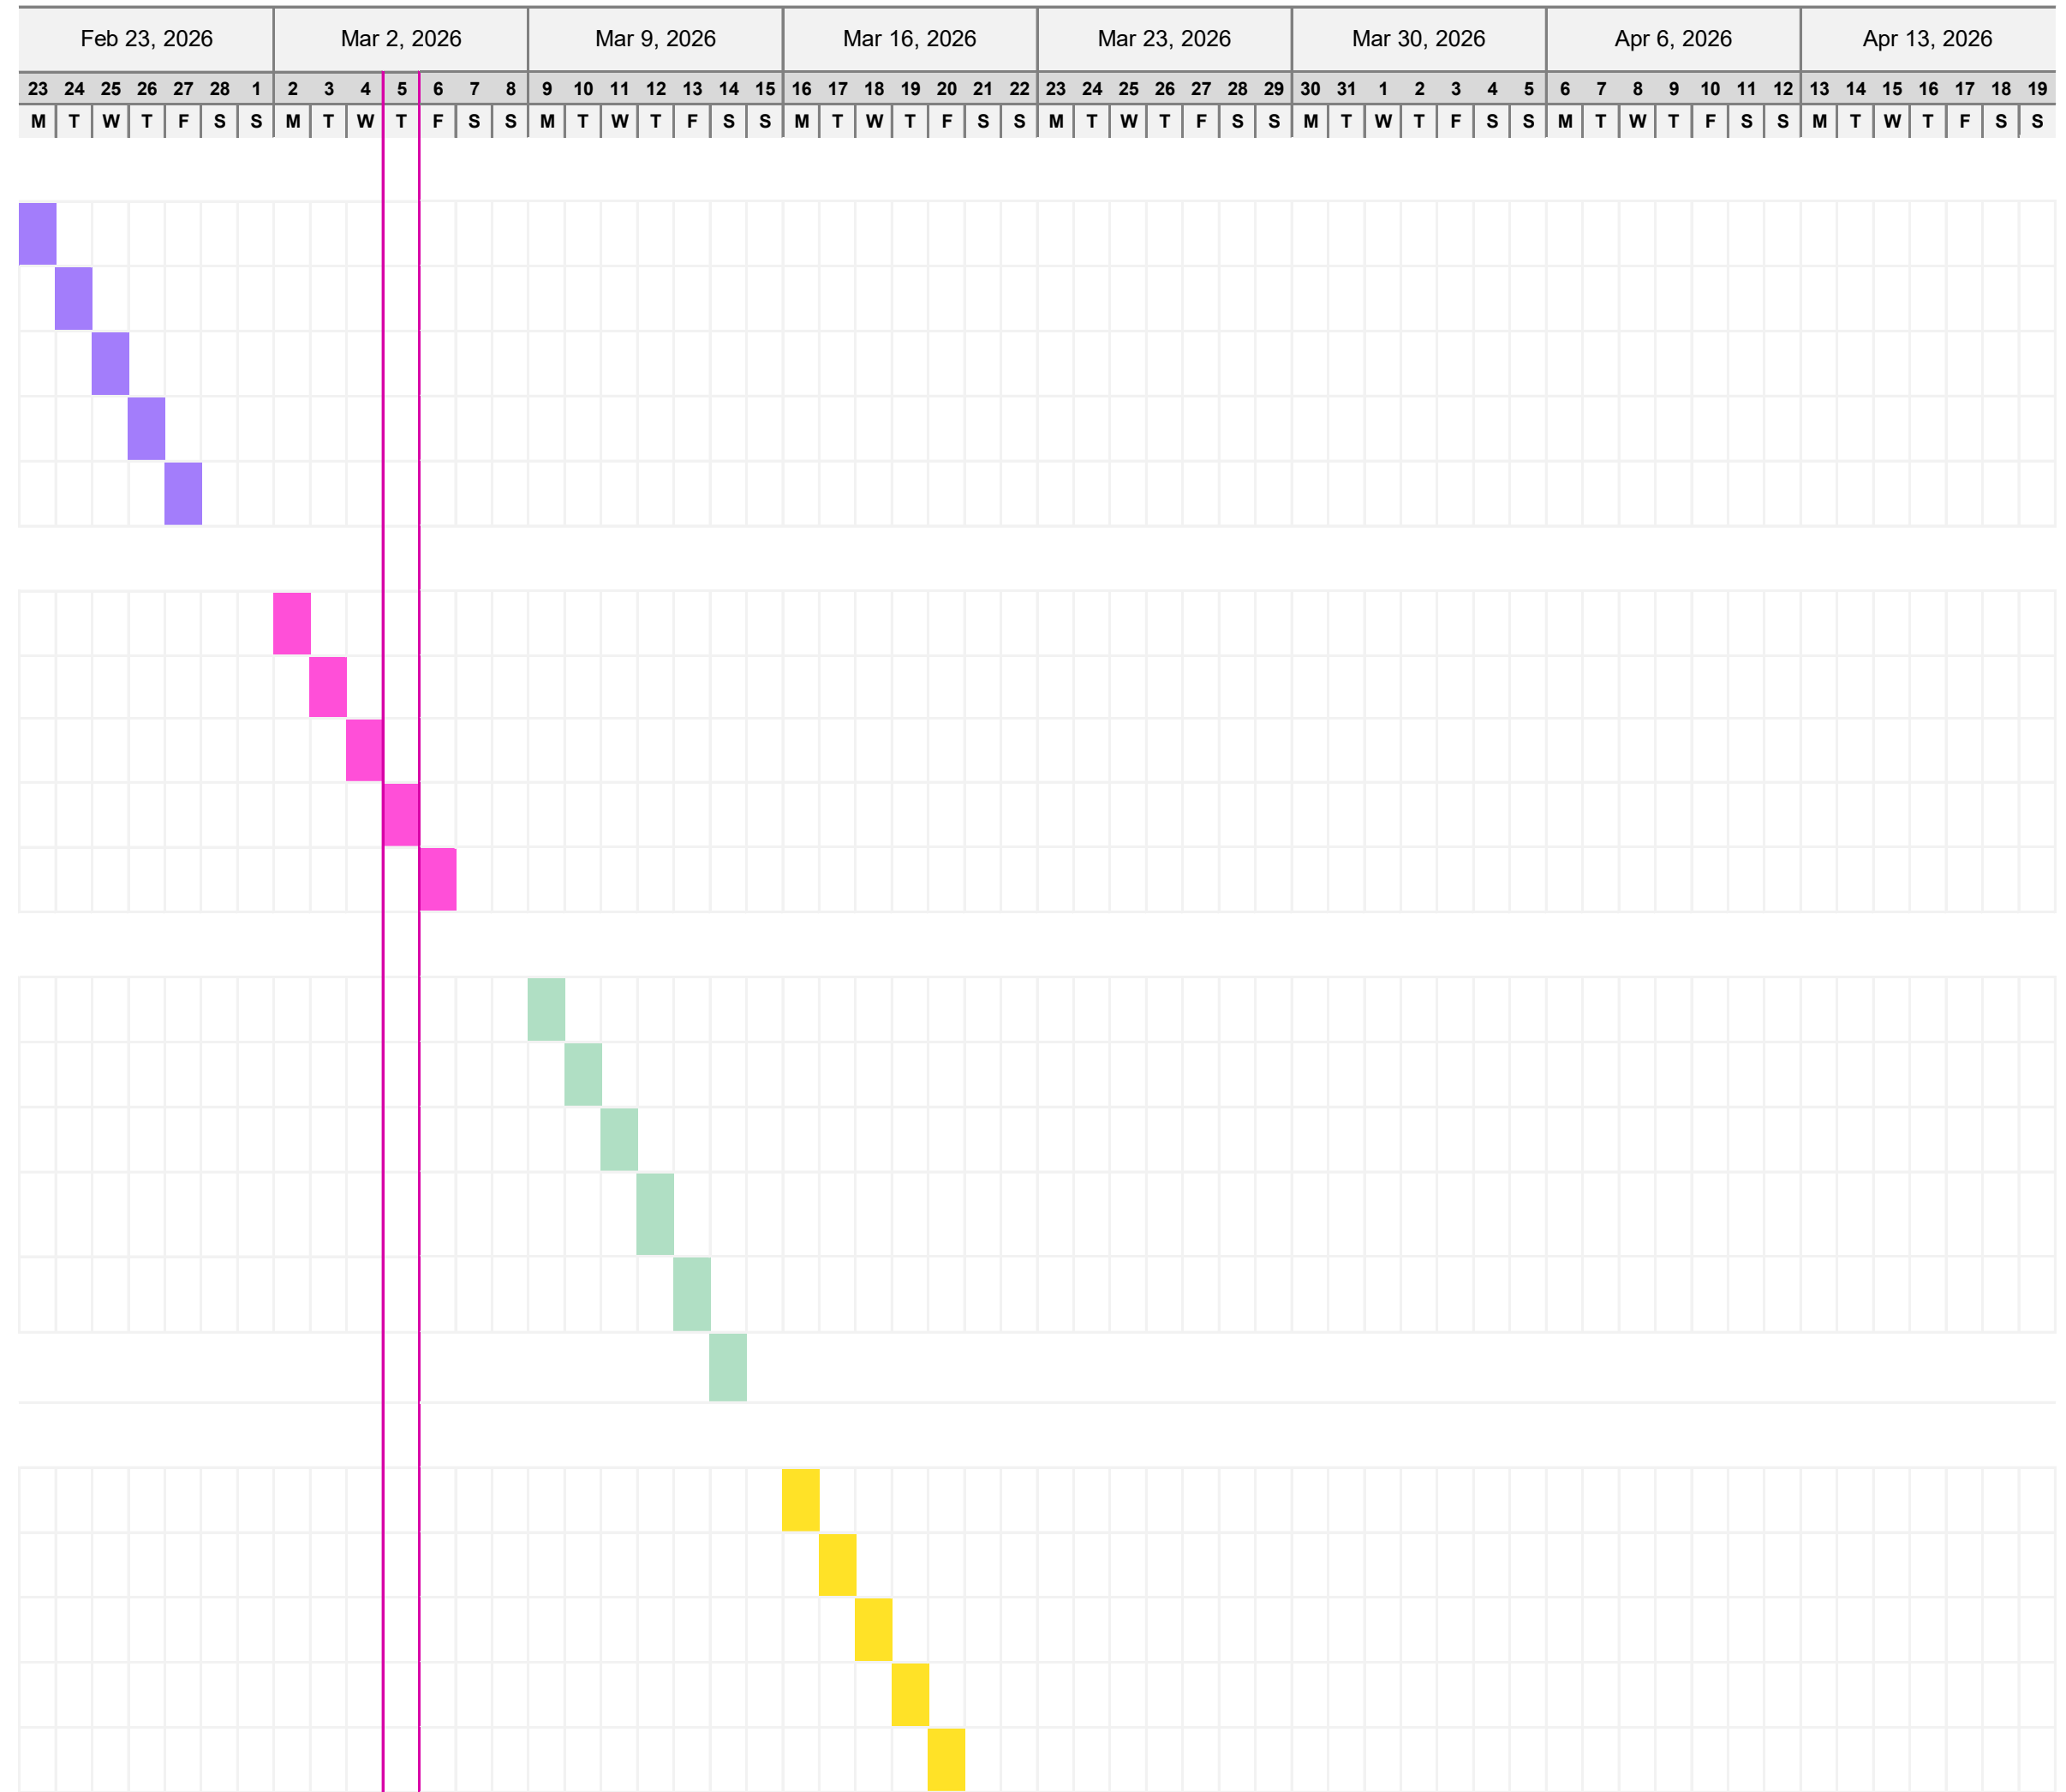

Insert new rows ABOVE this one
